

Universidad Politécnica de Aguascalientes

Project Plan

Medical Information System — Centralized Cloud Migration

Case Study: Centro Médico del Bajío

Subject:	IT Project Management — Unit II
Project Manager:	José Manuel Ortiz Medrano
Duration:	8 weeks (40 business days)
Timeline:	June 1 – July 31, 2026
Date:	June 26, 2026

1. Activity List

The project is broken down into 10 sequential activities on the critical path. Each activity lists its ID, description, predecessor, duration and responsible party. The baseline duration is 38 business days, leaving 2 days of slack within the 8-week (40 business-day) window.

ID	Activity	Pred.	Dur.	Responsible
C1	Define cloud hosting environment and storage requirements		3 d	PM, Cloud Specialist
C2	Analyze medical records and document types from the 3 branches	C1	4 d	PM, Medical Staff
C3	Design cloud database and storage architecture	C2	4 d	Cloud Specialist
C4	Evaluate cloud hosting providers (criteria table) and acquire digitalization equipment	C3	5 d	PM, Procurement
C5	Install and configure equipment in the 3 branches	C4	3 d	Implementation Team
C6	Digitize patient clinical records	C5	5 d	Digitization Team
C7	Digitize clinical analyses and complementary documents	C6	5 d	Digitization Team
C8	Migrate and upload digitized records to the cloud platform	C7	4 d	Cloud Specialist, IT
C9	Analyze and remove duplicate records	C8	3 d	IT Team
C10	Integration and validation testing	C9	2 d	PM, IT Team

Table 1. Project activity list. Critical path: C1→C2→C3→C4→C5→C6→C7→C8→C9→C10 (38 business days).

Budget Allocation per Activity

ID	Activity	Budget (MXN)
C1	Define cloud environment	8,000
C2	Analyze records	10,000
C3	Design architecture	12,000
C4	Provider selection + equipment	55,000
C5	Install equipment	12,000
C6	Digitize patient records	15,000
C7	Digitize analyses	15,000
C8	Migrate to cloud	10,000
C9	Remove duplicates	6,900
C10	Testing	4,000
	TOTAL (BAC)	147,900

Table 2. Budget allocation per activity (BAC = \$147,900 MXN).

2. Gantt Chart

The Gantt chart below shows the schedule of the 10 activities along the critical path, with the Week-4 review checkpoint (June 26) marked and the two slippage events reported at that meeting: the two-day sick-leave delay on C1 and the three-day extension on C6. The management target line indicates the go-live date moved one week earlier.

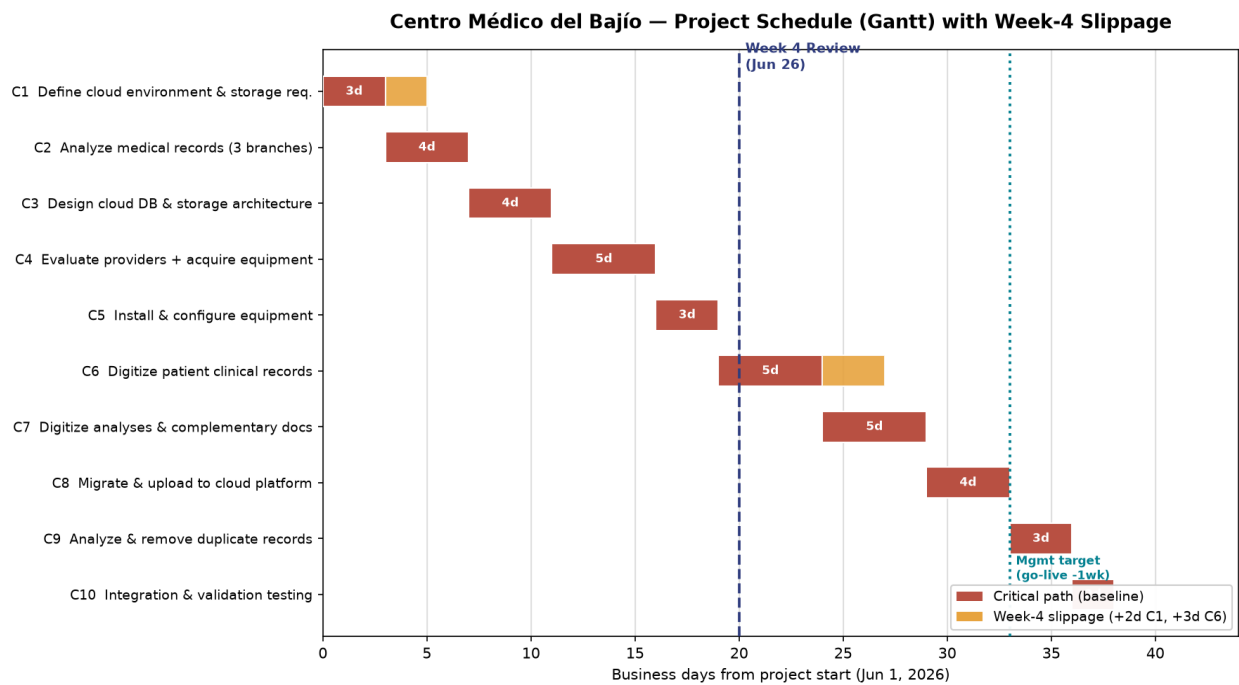


Figure 1. Project Gantt chart with Week-4 slippage overlay.

3. Project Closure Report

Hits (What Was Done Right)

- Successful deployment of the centralized cloud infrastructure (4 VMs, 32 GB RAM).
- 100% elimination of the 53,208 duplicated clinical records.
- Query response time achieved under 2.0 seconds across the 3 branches.
- The weighted criteria table gave an objective, defensible provider selection (Provider 1, 7.8/10).
- Change control absorbed the Week-4 disruptions without missing the July 31 go-live.

Failures (What Went Wrong)

- The initial activity (C1) was delayed 2 days by staff sick leave — no backup owner had been assigned.
- Three procurement deliverables were still pending at the Week-4 review.
- Activity C6 was underestimated — the patient-record volume required 3 extra days.
- The Earned Value formulas were initially recorded incorrectly (SV and CV swapped) and had to be corrected.

Improvements (For the Next Project)

- Assign a backup owner for every critical-path activity to absorb absences.
- Estimate digitization with a per-record parametric model instead of a flat duration.
- Pre-qualify vendors and lock delivery-time SLAs during Week 1.
- Standardize Earned Value templates so the SV and CV formulas cannot be swapped.
- Keep the short daily stand-up alignment meetings introduced during the rework.

Goals (Objective Achievement)

The strategic objective — consolidating the three branches onto a centralized cloud platform with 0% record redundancy, sub-2-second query response, within the \$147,900 MXN budget, and delivered by July 31, 2026 — was achieved at 100% compliance despite the disruptions reported at the Week-4 review. Corrective action through change control and the contingency reserve allowed the project to recover the schedule and meet all acceptance criteria.
